
modular project budgetary PROPOSAL

August 30, 2024

BOXX Project: Q-77117





City of Port Saint Lucie

2195 SE Airso Blvd Port St Lucie, FL 34984

Engineering Plan per specifications

BOXX Modular, Inc. (Corporate Office) 3475 High River Road | Fort Worth, TX | 76155







P: (772) 775-4162

C: +1 7727754162

icollins@boxxmodular.com



August 30, 2024

Carrie Wilbur
City of Port Saint Lucie
121 SW Port St. Lucie Blvd.
Port St. Lucie, Florida 34984

RE: Modular project in Port St Lucie, FL

Dear Carrie.

I am very pleased to have the opportunity to submit this proposal which has been carefully tailored to address your individual space requirements.

BOXX Modular has been committed to providing quality products, services, and customer satisfaction to both the public and private sectors since 2010. Our expertise in development and execution of wide-ranging space solutions affords us the distinct satisfaction of fulfilling each of our client's modular construction needs.

Proposal Contents (attached):

Engineered plans for Permitting

It is our goal to meet your specific needs, so please be certain to thoroughly review each attachment included in this proposal to ensure you completely understand the pricing, product, and service we are proposing.

Please do not hesitate to contact me for answers to any questions or concerns you may have regarding our proposed solution. It would be our pleasure to partner with you on this important project. Thank you for your consideration.

Sincerely,

Jane

Jane A Collins

modular project Sale Price Detail

This proposal is valid for 10 calendar days

BASE PRICE

Scope of Work Description

Engineered plans for Permitting

1 set.

Digital Stamped Plans Set

Amount (usd)

7500.00

1000.00

*Base Price Total:

TBD

OPTIONS

Initials = Selected


Option Description


Amount (usd)


PROJECT DESCRIPTION DETAIL

Complete Stamped Engineered plans for permitting process.

Pricing excludes all applicable taxes. Buyer is responsible for all applicable taxes. Proposal Price does not include sales, use, or personal property taxes, except as may be additionally described. Unless otherwise specified, Proposal is valid for 10 calendar days from the "Proposal Date". BOXX Modular's willingness to enter into a contract at the price and/or terms of payment proposed is contingent upon satisfactory credit review and approval. Pricing is based on acceptance of BOXX's standard contract terms and conditions, along with timely receipt of any contractually required down payment.




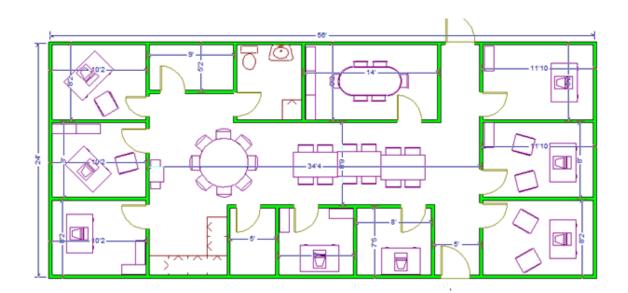




modular project Delineation of Responsibilities

Division	Sub	Description	вохх	Owner	NA
DIVISION 1 : GEN	IERAL CO	ONDITIONS			
	1011	Performance Bonds			X
	1040	Building Permits/License		X	
	1500	Temporary Heat/Lighting		X	
		Portable Toilets		X	
		Temporary Water & Power		X	
	1502	Site Cleanup/Dumpster	X	X	
	1700	Closeout/Acceptance	X		
	1900	Miscellaneous	X		
		Taxes		Х	
		Prevailing Wage Scale (Davis-Bacon)			Х
		Safety and Security Access Requirements For Workers		Х	
		Project Terms of Payment	Х		
		Invoicing Procedure	Х		
DIVISION 2 : SIT	E WORK				
	2000	Site Work		Х	
		Accessibility		Х	
		Stake Site/Building Location		Х	
	2160	Excavation & Grading		Х	
		Spoilage Disposal		Х	
		Erosion Control		Х	
	2660	Final Connection of Domestic Water To Building			
		(including modular seam crossover piping in ceiling)		Х	
	2740	Final Connection of Sewer To Building (including manifolds in crawlspace and vents thru roof)		х	
	2900	Landscaping / Fine Grading		X	
	2000	Seeding		X	
		Restoration		X	
DIVISION 3 : Con	crete (SIT			Α	
	3300	Foundations		Х	
DIVISION 5 : Meta					
	5000	Decks/Landings/Ramps (Engineered Aluminum)			TBD
DIVISION 6 : WO		STIC (SITE ONLY)	1	I	
	6670	Decks/Landings (Pressure Treated Wood)			TBD
DIVISION 9 : FINI					
	9650	VCT Flooring with / without carpet bar	Х		
	9680	Carpeting with / without carpet bar			Х
	2000		l .	ı	



modular project Delineation of Responsibilities

Division	Sub	Description	вохх	Owner	NA
DIVISION 10 : SP	ECIALTIE	S (SITE ONLY)			
	10100	Marker/Chalk/Tack Boards		Х	
	10425	Signage/Braille		X	
	10520	Fire Extinguishers		Х	
	10532	Awnings		Х	
	10800	Toilet Accessories		Х	
DIVISION 13 : BU	ILDING (N	MODULAR BUILDING)			
	13121	Delivery Of Modular Units To Site Including Transp. Permits	Х		
	13122	Piers			Х
		Dry-Stack Block/Steel Piers On ABS Pads	Х		
		Surface Bond Dry Stack			Х
	13123	Set-up	Х		
		Structurally Connect Modular Floors & Roofs	Х		
		Remove Hitches (Store Under Bldg. If stored in different			
		location, may be an additional cost)	Х		
	40405	Trim Out Exterior & Interior Walls/ Ceiling/Floors/Adjust	v		
	13125	Doors	X		
	13126	Anchor Modular Units Per Design Criteria Skirting to match building (Frame, Venting, Access Panel	Х		
	13127	Included)	Х		
	13128	Roof Seaming	Х		
	13151	Site Construct Connector Corridors			Х
DIVISION 16 : EL		·	<u> </u>	I I	
	16410	Connect Electrical Service From Site to Modular Subpanels		Х	
		Main Disconnect For Modular Building Connection		Х	
		Supply and Install MDP		Х	
	16610	Fire / Smoke Alarm Systems		Х	
	16620	Security Intrusion System		Х	
	16740			Х	
	16750	Communication Systems in Modular		Х	
		Tap & Extend Existing Comm Service To Site		Х	
		Final Connection of Comm System in Modular		Х	
	16770	Data Systems in Modular		Х	
		Tap & Extend Existing Data Service To Site		X	
		Final Connection of Data System in Modular		X	
	I .	1 55. modion of Bata Gyotom in Modular	1		



modular project Schedule

This proposal is valid for 10 calendar days


TIMELINE

Estimated Completion
Engineered plans 4 weeks
from payment

Milestone Description

SCHEDULE NOTES

Additional Information




modular project Terms & Exclusions

Terms

- 1. Unless otherwise specified, Proposal is valid for 10 calendar days from the "Proposal Date". Building costs and production schedules change daily. At expiration of validity period Price and Delivery are subject to change without notice until Proposer accepts Order.
- 2. BOXX's willingness to enter into a contract at the price and/or terms of payment proposed is contingent upon satisfactory credit review and approval
- 3. Proposal pricing and project schedule is based on acceptance of BOXX's standard contract terms and conditions, along with timely receipt of any contractually required down payment.
- 4. Any Project Schedule provided with the Proposal is an estimate. Project Schedule will be confirmed at or around the time of Award, and may be subject to change orders throughout the Project.
- 5. Unless otherwise agreed in writing, BOXX will not accept any Liquidated or other damages for delays.
- 6. Prior to start of its Work, BOXX shall provide a proper Certificate of Liability Insurance and Worker's Compensation. Unless otherwise agreed in writing, "All Risk" and other special insurance is not provided by BOXX. As of the time of Substantial Completion, or as otherwise agreed, Buyer shall be responsible to insure the building(s), providing insurance coverage in the types and limits as may be required by the contract to adequately protect the interests of all applicable parties.
- 7. Buyer is responsible for all applicable taxes. Proposal Price does not include sales, use, or personal property taxes, except as may be additionally described. Customer is responsible for paying a personal property fee of eight percent (8%) of the monthly rent (or lease) payment to BOXX.
- 8. Unless otherwise agreed to in advance as a condition of the Contract, price assumes the use of non-union labor at non-prevailing wages. Any requirement for the payment of prevailing wages or the use of union labor will result in additional charges.
- BOXX will take reasonable protective precautions to avoid damage to property and equipment. BOXX will not accept responsibility for damage caused to
 paved or unpaved surfaces due to weight of heavy equipment.
- 10. TITLE BOXX Modular, Inc. will retain title to the work until such time that they have been paid in full for the delivery, installation and either direct sale or receipt of all amounts due to complete the finance lease of the building(s). BOXX does not waive its rights to retain title and/or to place a lien or claim against the Owner/Buyer/Lessee if it becomes reasonably necessary in order to protect BOXX's interests.
- 11. INDEMNIFICATION BOXX Modular, Inc. will indemnify Owner/Buyer/Lessee to the extent that they are legally responsible and permitted by BOXX's insurance carrier.
- 12. START AND COMPLETION DATES The contract Start Date shall be upon receipt of award and an executed contract. Barring any unforeseen delays, The Completion Date will be in accordance with bid specifications and the attached Schedule (to be confirmed upon receipt of award). BOXX is not responsible for any delays or damages beyond its control including material shortages, strikes or union activity, fire, acts of God, freight embargoes, acts of war or terrorism, delays by regulatory or permit authorities, delays by the Owner or Architect or any employed by them, or any cause of delay beyond the control of BOXX. In no event shall BOXX be responsible for consequential or actual damages.
- 13. Labor will be non-union at non-prevailing wages unless required by contract

Exclusions


Exclusions	
X = Excluded	
X	1. Impact fees
X	2. All applicable taxes (sales, property & use)
X	3. Bonding
X	4. Special insurance
X	5. Cranes and additional spotting apparatus
X	6. Fire suppression system
X	7. Site security (unless otherwise stated)
X	8. Landscaping, irrigation, paving, walkways, curbing, and site restoration
X	9. Tap fees and lift station (if required)
X	10. Exterior fire rating
X	11. Architect and engineering fees
X	12. Rock removal
X	13. Off-site spoilage removal
X	14. Site utilities and connections to modular building – includes electric, gas, water, and sewer or septic
X	15. Communications services and connection – including but not limited to telephone, data, intercom, intrusion alarm, smoke & fire alarm
X	16. Lightning protection
X	17. Temporary access roads and walkways
X	18. Removal, repair, and/or replacement of obstructing fences, walls or gates
X	19. Temporary electric and water (contractor will supply power source for own tools and equipment)
X	20. Portable toilets
X	21. Laboratory and field testing of materials
X	22. Dedicated full-time site supervisory personnel (foreman will supervise work unless other provisions are required per the contract)
X	23. Costs associated with easement(s)



modular project Site Requirements

Site Requirements

X = Applicable	
X	1. No provisions allowed for obstructions below grade. If encountered, they would be a change order to the contract at an additional charge
X	2. The site must be level, dewatered, and accessible by truck with adequate turning radius and clearance from road to the site for delivery
X	3. Assumes site with 2,500 psf soil bearing capacity, bearing tests to be provided by Customer
X	4. All site plans and surveys to be provided by Customer
X	5. All underground utilities are to be clearly marked and flagged
X	6. Customer is responsible for obtaining and the cost of all permits, licenses, and Certificate of Occupancy
X	7. Due to volatility in fuel prices delivery charges are subject to a fuel surcharge.
X	8. Staging area adjacent to installation site, including any site improvements required to make it usable, by Customer
X	9. Where applicable, wheels and axles will remain on module(s), but may be removed and stored under for an additional fee
X	10. Site preparation by Customer
X	11. Building removal, return delivery, and site restoration will be billed at prevailing rates at time of return
X	12. Main electrical service to building panels by Customer
X	13. Customer is solely responsible to inform BOXX Modular if site location is in a flood or fire zone
X	14. Customer is responsible for building maintenance



References

Available upon request



modular project Proposal Acceptance

This proposal is valid for 10 calendar days due to rapid and unpredictable cost increases.

Pricing and project schedule is based on acceptance of BOXX's standard contract terms and conditions, along with timely receipt of any contractually required down payment.

City of Port Saint Lucie

August 30, 2024

Signature Print Name Acceptance Date

BOXX Modular builds for you!





		APPLICATION FOR CREDIT	
Α	Legal Name of Company/Organization Street Address	B Sole Proprietor S Corporation Partnership Other State Registered:	LLC Non-profit
	Suite City, State, ZIP Phone	Fax	Email
	DUNS#	Federal ID/Social Security Number	Company Owner's Name
С	State Sales/Use tax: Taxable ☐ PO Required? Yes ☐ No ☐ (If Yes, att Billing information (if different from above)	Exempt [] (Exemption Certificate must be a tach PO Terms and Conditions)	attached)
	Mailing address	Contact Name (Accounts Paya	able)
	Suite/Box	Email (Accounts Payable)	
	City, State, ZIP	Phone (Accounts Payable)	······································
·			
D	Intended use for modular(s):	Property Owner Na	ame:
D	Intended use for modular(s): Property Ownership: The project location is Landlord Waiver (if Leased / Rented): N	is Leased / Rented Applicant Owned	Property Address:
D E	Property Ownership: The project location is Landlord Waiver (if Leased / Rented): No	is Leased / Rented Applicant Owned eed A Copy Executed & Attached ore quickly please provide the following info # of Employees:	Property Address:
E	Property Ownership: The project location is Landlord Waiver (if Leased / Rented): No	is Leased / Rented	Property Address:
	Property Ownership: The project location is Landlord Waiver (if Leased / Rented): No	is Leased / Rented Applicant Owned eed A Copy Executed & Attached ore quickly please provide the following info # of Employees: ACH Pmts: Yes No No NOTE: PHONE, FAX NUMBERS OR EMA	Property Address:
E	Property Ownership: The project location is Landlord Waiver (if Leased / Rented): No	is Leased / Rented Applicant Owned eed A Copy Executed & Attached ore quickly please provide the following info # of Employees: ACH Pmts: Yes No NOTE: PHONE, FAX NUMBERS OR EMA Acct. #:	Property Address: Drmation with your application: Bank Statements – Last 3 months AILS ARE REQUIRED!
E	Property Ownership: The project location is Landlord Waiver (if Leased / Rented): No	is Leased / Rented Applicant Owned eed A Copy Executed & Attached ore quickly please provide the following information with the form of credit at the time of any renewal or extension of credit, or when applicant, its directors, and officers, who did sign be ion, use, sharing and disclosure of its information by Board or withhold, cancel or modify credit privileges and terms.	Property Address: Description with your application: Bank Statements — Last 3 months ALLS ARE REQUIRED! Contact: Treports or other, relating to the applicant, as the case then deemed appropriate to evaluate the applicant's elow declare and warrant that he/she/they is/are the age OXX Modular Inc. (or any of its affiliates) for the above time, including the rate of interest at their discretion.
E	Property Ownership: The project location is Landlord Waiver (if Leased / Rented): No No Notice: BOXX Modular Inc. (or any of its affiliate may be upon processing the initial application, a financial situation. In signing this application, the of majority and expressly consent to the collections tated purposes. 2. BOXX Modular Inc. reserves the right, at any time Authorization Signature:	is Leased / Rented Applicant Owned eed A Copy Executed & Attached ore quickly please provide the following information with the following information in the form of credit at the time of any renewal or extension of credit, or where applicant, its directors, and officers, who did sign be ion, use, sharing and disclosure of its information by BO	Property Address: Drmation with your application: Bank Statements — Last 3 months AILS ARE REQUIRED! Contact: Treports or other, relating to the applicant, as the case then deemed appropriate to evaluate the applicant's elow declare and warrant that he/she/they is/are the age OXX Modular Inc. (or any of its affiliates) for the above trms, including the rate of interest at their discretion. Date: Date:

THIS PAGE INTENTIONALLY LEFT BLANK
