

Enter RFP Information on the "Summary" page

Evaluation Summary	
RFP #:	
RFP Name:	
Issuing Officer:	
Point Difference for Competitive Range:	

Spreadsheet columns hi-lited in purple have formulas. If you change the formulas, the spreadsheet will not work.

Do not erase or modify these cells		
Rating	Factor	
Poor	0	
Marginal	0.25	
Adequate	0.5	
Good	0.75	
Excellent	1	
No Response	0	

Enter each offeror's name in the Offeror Name column. The names will flow to the appropriate worksheet.

Enter each offeror's Cost Score in summary once technical evaluation is completed.

Offeror Name	Graph #	Cost Score	Average Initial Score	Average Validated Score	Final Score (Cost + Validated)
Offeror #1	1		0.00	0.00	0.00
Offeror #2	2		0.00	0.00	0.00
Offeror #3	3		0.00	0.00	0.00
Offeror #4	4		0.00	0.00	0.00
Offeror #5	5		0.00	0.00	0.00
Offeror #6	6		0.00	0.00	0.00
Offeror #7	7		0.00	0.00	0.00
Offeror #8					
Offeror #9					
Offeror #10					
Offeror #11					
Offeror #12					
Offeror #13					
Offeror #14					
Offeror #15					
Offeror #16					
Offeror #17					
Offeror #18					
Offeror #19					
Offeror #20					


	1	2	3	4	5	6	7	8	9	10	11	12
Cost Score												
Average Initial Score	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Average Validated Score	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

These spreadsheets are designed to hold 300 questions. If you have more questions than that, you can add them in rows 320 and below. However, you must be sure to do the following in order for the spreadsheet to work properly.

- 1 On Offeror #1 spreadsheet, enter your Question Types, Question #s, Questions, Answers, and Possible Points in columns A through E, respectively. Note that the Question Types must be all caps - AS or MS.
- 2 On Offeror #1 spreadsheet, before entering anything in the Validated Rating columns, copy columns I through FQ down to the last row of questions. This will copy the drop-down list in the Validated Ratings columns and the formula in the Validated Score columns.
- 3 On all other Offeror spreadsheets (# 2 through #20), copy columns A - FQ down to the last row that should have questions. This will copy the formulas needed to show the information entered on the Offeror #1 spreadsheet on all spreadsheets. It will also copy the Validated Rating drop-down list and the Validated Score formula. For example, if Offeror #1 spreadsheet has questions on rows 320 through 340, copy columns A - FQ down to row 340 on all other Offeror spreadsheets. The Question Type, Question #, Question, Answer, and Possible Points will now display on the other Offeror spreadsheet.

Offeror Name
Offeror #1

Right-click on the tab name, select "Rename" from the pop-up menu and enter the offeror's name



Using the drop-down list in the Question Type column to mark the question as either Mandatory Scored (MS) or Additional Scored (AS).  
On the Offeror #1 worksheet, copy and paste the Question #, the text of the question, and the possible points. Entries will display on other Offeror worksheets.

Question Type	#	Question	Answer	Possible Points

Copy and paste each individual offeror's answer into the Answer column on the worksheet for that offeror.

Enter the name of the team member doing the evaluation here. Each worksheet can have up to 20 evaluators.

**Step #1** -- Copy the Initial Rating column on the Individual Evaluation Workbook and paste into the Initial Rating column of the Master Workbook

**Step #2** -- Copy the Initial Score column of the Individual Evaluation Workbook and copy into the Initial Score column of the Master Workbook by using "Paste Special" -- Right click, select "Paste Special..." and click the "Values" radio button, and then OK.



See diagram to the right →

**Step #3** -- Copy the Initial Comments column on the Individual Evaluation Workbook and paste into the Initial Comments column of the Master Workbook.

Select Validated Rating from the drop-down list and enter Validated Comments. Validated Score calculates automatically.


Initial Rating	Initial Score	Initial Comments	Validated Rating

Initial and Validated Scores automatically display in these cells and on the Summary tab



<b>Evaluation Summary</b>	
<b>RFP #:</b>	<b>20210022</b>
<b>RFP Name:</b>	<b>Design &amp; Permitting of the Western 30" &amp; 24" Raw Water Main Projects</b>
<b>Issuing Officer:</b>	<b>Jason Bezak</b>

<b>Offeror Name</b>	<b>Graph #</b>	<b>Initial Score</b>	<b>Validated (Final) Score</b>
CAPTEC Engineering, Inc.	1	658	679
Culpepper & Terpening	2	633	654
Kimley-Horn and Associates, Inc.	3	646	717
<b>NOT SHORTLISTED</b> - Chen Moore and Associates	4	588	N/A
<b>NOT SHORTLISTED</b> - CivilSurv Design Group, Inc.	5	592	N/A
<b>NOT SHORTLISTED</b> - Holtz Consulting Engineers,	6	613	N/A

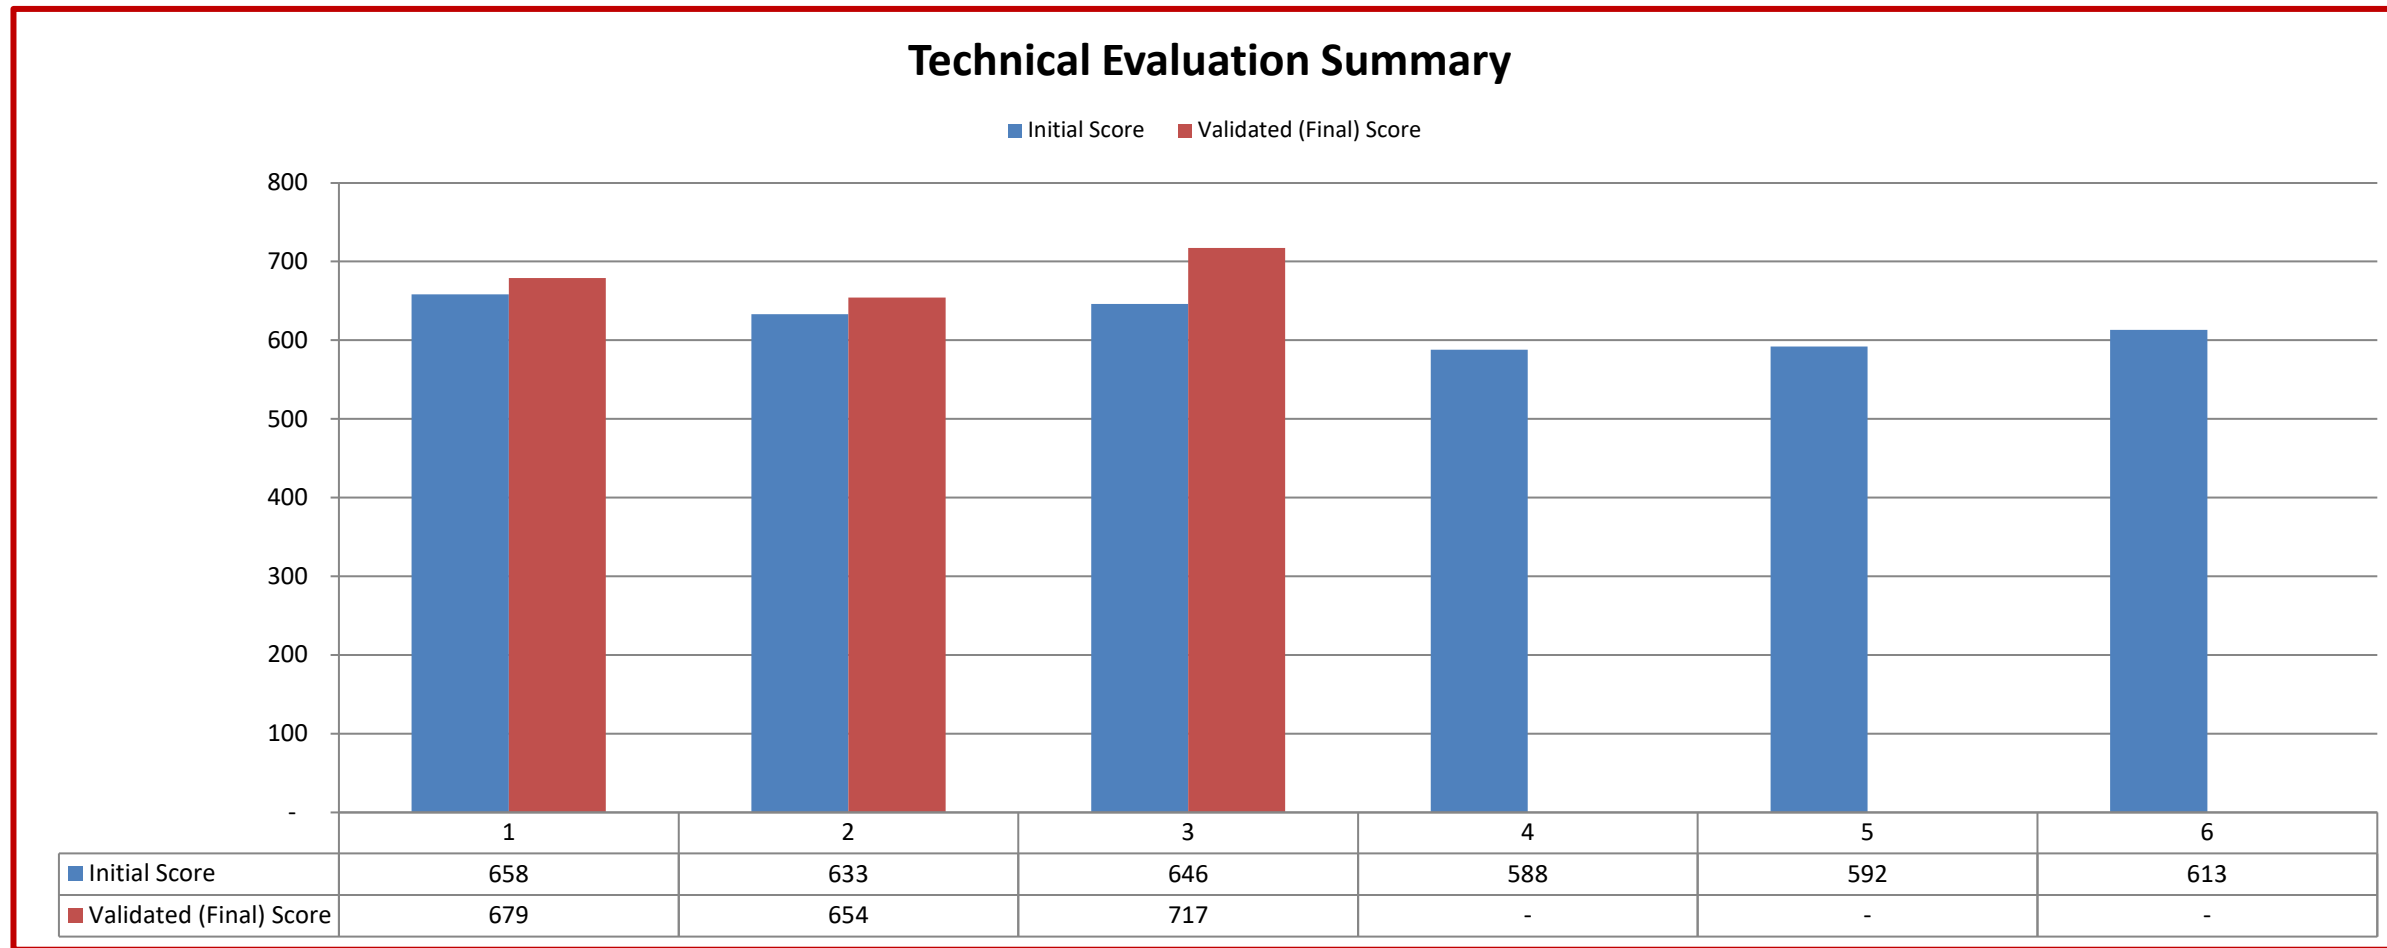

Master Technical Evaluation Template  
 RFP #: 20210022  
 RFP Name: Design & Permitting of the Western 30" & 24" Raw Water  
 Issuing Officer: Jason Bezak  
 Date Reviewed:

Reminder - Do not change formulas in Validated Score columns.

Offrort Name	Average Initial Rating	658.33
CAPTEC Engineering, Inc.	Average Validated Score	679.17

Question and Point information entered in columns A - C will flow to other tabs. Evaluator names will flow to other tabs. Rows 12 thru 18 are hidden on all tabs. Do not unhide these rows. Do not change the formulas on these rows or the spreadsheet will not work.

Question Type	#	Question	Answer	Possible Points	Bilmer Serrano					Daniel Burdett					David Garland							
					Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score
	1	Please provide all documentation needed for Location. Proposer's Location - Location shall mean a business which meets the following criteria: # of Miles from City Hall to Assigned Staff's Office location 0-60 Miles 61-80 Miles 81-100 Miles 101-120 Miles 121-140 Miles 140+ Miles	Yes, CAPTEC Engineering, Inc. is located within 9 miles of City Hall.	50	Excellent	50.00	Procurement has verified this item.	Excellent	Procurement has verified this item.	50.00	Excellent	50.00	Procurement has verified this item.	Excellent	Procurement has verified this item.	50.00	Excellent	50.00	Procurement has verified this item.	Excellent	Procurement has verified this item.	50.00
	2	Woman/Veteran/Minority Owned Business: Does the Primary firm hold a Minority Business Certification by the Florida Department of Management Services, as described in section 8 of the document? If so, please attach.	No, CAPTEC Engineering, Inc. is not a Minority Owned Business.	100	Poor	0.00	Procurement has verified this item.	Poor	Procurement has verified this item.	0.00	Poor	0.00	Procurement has verified this item.	Poor	Procurement has verified this item.	0.00	Poor	0.00	Procurement has verified this item.	Poor	Procurement has verified this item.	0.00
	3	Executive summary. This section should include the Firm's overall concept of the working relationship that will be required to successfully complete this project. The proposer shall provide an executive summary narrative containing information that indicates an understanding of the overall need for and purpose of the services presented in the RFP.	Yes	50	Good	37.50	Experience with personnel and projects in area.	Good	Experience with personnel and projects in area.	37.50	Good	37.50	long working relationship with PSL.	Good	long working relationship with PSL.	37.50	Excellent	50.00	Provided statements about staff and capabilities of the firm. Submitted their understanding of the project scope. Can provide grant funding experience.	Excellent	Excellent staff. Qualified in all aspects of project from design through permitting, easements and construction services. Capable of producing high quality results.	50.00
	4	Project plan. A project plan is a formal document designed to guide the control and execution of a project. A project plan is the key to a successful project and is the most important document that needs to be created when starting any business project. This should include any special concerns or accommodations needed for a successful project. The plan shall also include methods for planning, organizing, scheduling, coordinating, and administering the total effort. Explain the overall approach to the project.	Yes	200	Good	150.00	Understands importance of obtaining proper field data	Good	Understands importance of obtaining proper field data	150.00	Adequate	100.00		Good	City can pick project manager	150.00	Good	150.00	Nice, to the point discussion of their project plan. Discussed how they'll handle every phase of the project.	Good	Review of alternative routes. Prepare a final route plan after acceptance by City. Prepare dwgs., procure permits and complete design within 480 day project timeline. Able to fast-track project to shorten design time. Will pursue easements starting at the NTP and are familiar with the canal route.	150.00
	5	What does your firm anticipate being the most challenging part of this project?	Yes	100	Adequate	50.00		Adequate		50.00	Adequate	50.00		Marginal	Had an issue with a	25.00	Good	75.00	Listed route selection and	Excellent	Wetlands may require	100.00
	6	Provide a listing of firm's current contracts.	Yes	50	Adequate	25.00		Adequate		25.00	Excellent	50.00	extensive list of current contracts	Excellent	extensive list of current contracts	50.00	Good	37.50	Listed projects for drainage, sidewalks, and McCarty Ranch Water Quality Ponds.	Good	Good variety of local projects including PSLUSD.	37.50
	7	Please complete and attach Form 330 part I and II for evaluation of qualifications & staff/personnel.	Yes	100	Adequate	50.00		Adequate		50.00	Excellent	100.00	well defined qualifications	Excellent	well defined qualifications	100.00	Excellent	100.00	Excellent staff with experience with large diameter pipelines.	Excellent	Excellent staff with experience with large diameter pipelines.	100.00
	8	Value-added services. This term is used for non-core services, or all services beyond the identified scope. Does the firm recommend any optional value-added services?	Yes	50	Good	37.50	Experience in horizontal directional drilling	Good	Experience in horizontal directional drilling	37.50	Adequate	25.00		Adequate		25.00	Excellent	50.00	HDD experience. Local pipeline projects with large diameter pipe. Great construction engineering service. Experience with rancher leases. Previous work on LTC Ranch pipeline route analysis and FPL ROW.	Excellent	Experience with rancher leases. Previous work on LTC Ranch pipeline route analysis and FPL ROW.	50.00
	9	Proposed Schedule. Making adjustment for issues that may arise during this project, what is your proposed schedule for this project? This section shall include a detailed breakdown and timelines for achieving the scope of work, with a delineation of assigned staff for each task associated with the project. Also include quality assurance efforts for the data collection and analysis tasks, a process for ensuring that no individual respondents will be identified, and a project timeline. The consultant must have sufficient equipment and personnel for back-up and/or emergencies to ensure prompt scheduling and completion of services within the schedule. Final project schedule will be negotiated with awarded firm.	Yes	100	Adequate	50.00		Adequate		50.00	Excellent	100.00	seems to get projects completed on time or earlier.	Excellent	seems to get projects completed on time or earlier.	100.00	Good	75.00	Concise proposed schedule covering staffing required for each task. Sufficient staff available. QC by principal engineer. Project completion within 12 to 16 months.	Excellent	They have recently completed a similar project. They will use concurrent work tasks to comply with the limited time frame. Route analysis, FPL coordination, and easements with property owners could be done during preliminary design phase. Upon selection of the route, environmental survey and geotechnical work will be done. FDEP permit, FDOT permit, and County ROW permit following the 60% plans submittal. Final easements will be obtained during the start of the 90% plans. Construction services starting with shop drawing reviews to start	100.00
	10	Other Material. Please include any additional material that may assist the City in evaluating the proposals and approach to the project. Pre-printed advertisements, brochures, and promotional material may be attached as additional information, but shall not serve as a substitute for a specific response. Attachment of brochures instead of the written response request will be grounds for disqualification or devaluation. A simple "yes" or "no" answer alone will not be acceptable unless clearly requested; an explanation shall be provided for each question/issue listed in this response outline. However, clarity and brevity of presentation, not length, will be favorably considered.	Yes	50	Good	37.50	Experience in this location	Good	Experience in this location	37.50	Adequate	25.00		Adequate		25.00	Excellent	50.00	Previous work with PSLUSD. Staff availability. Local experience. QC during all phases. Very good CEI staff.	Excellent	Previous work with PSLUSD with outstanding CEI services. Familiar with ranch leases on LTC Ranch that allow for agricultural exemptions to Owners. Previously performed survey for Canal C-104 and the FPL easement.	50.00
	11	Innovation. Please outline any tools in the firms "toolbox" that can be considered innovative and that have proven to benefit the successful completion of similar projects recently.	Yes	50	Adequate	25.00		Adequate		25.00	Adequate	25.00		Adequate		25.00	Good	37.50	Use of drones. Customer complaint hotline. Value engineering.	Adequate		25.00
	12	Company Experience. Please outline and elaborate on your company's experience with projects similar to this project that included residential construction areas, FDOT permitting, Horizontal directional drilling and large diameter force main (24" or larger).	Yes	100	Good	75.00	Recent experience of 24" force main project	Good	Recent experience of 24" force main project	75.00	Adequate	50.00		Adequate		50.00	Excellent	100.00	Excellent staff experience with large diameter pipelines for PSLUSD including HDD, FDOT and FDEP permits, and construction services. Survey and geotech coordination as well as preparation of easement documents.	Excellent	Excellent staff experience with large diameter pipelines for PSLUSD including HDD, FDOT and FDEP permits, and construction services. Survey and geotech coordination as well as preparation of easement documents.	100.00

Master Technical Evaluation Template

RFP #: 20210022  
 RFP Name: Design & Permitting of the Western 30" & 24" Raw Water  
 Issuing Officer: Jason Bezak  
 Date Reviewed:

Reminder - Do not change formulas in Validated Score columns.

Offeror Name  
 Culpepper & Terpening

Average Initial Rating 633.33  
 Average Validated Score 654.17

Question and Point information entered in columns A - C will flow to other tabs. Evaluator names will flow to other tabs. Rows 12 thru 18 are hidden on all tabs. Do not unhide these rows. Do not change the formulas on these rows or the spreadsheet will not work.

Question Type	#	Question	Answer	Possible Points	Bilmer Serrano					Daniel Burdett					David Garland							
					Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score
	1	Please provide all documentation needed for Location. Proposer's Location - Location shall mean a business which meets the following criteria: # of Miles from City Hall to Assigned Staff's Office location 0-60 Miles 61-80 Miles 81-100 Miles 101-120 Miles 121-140 Miles 140+ Miles	2980 S. 23th Street, Fort Pierce, Florida 34981	50	Excellent	50.00	Procurement verified this item.	Excellent	Procurement verified this item.	50.00	Excellent	50.00	Procurement verified this item.	Excellent	Procurement verified this item.	50.00	Excellent	50.00	Procurement verified this item.	Excellent	Procurement verified this item.	50.00
	2	Women/Veteran/Minority Owned Business: Does the Primary firm hold a Minority Business Certification by the Florida Department of Management Services, as described in section 8 of the document? If so, please attach.	NO	100	Poor	0.00	Procurement verified this item.	Poor	Procurement verified this item.	0.00	Poor	0.00	Procurement verified this item.	Poor	Procurement verified this item.	0.00	Poor	0.00	Procurement verified this item.	Poor	Procurement verified this item.	0.00
	3	Executive summary. This section should include the Firm's overall concept of the working relationship that will be required to successfully complete this project. The proposer shall provide an executive summary narrative containing information that indicates an understanding of the overall need for and purpose of the services presented in the RFP.	See detailed response in attachment.	50	Good	37.50	Experience working with city personnel	Good	Experience working with city personnel	37.50	Adequate	25.00		Adequate		25.00	Excellent	50.00	Extensive experience with the City, FDOT and FPL. Currently, design engineer for LTC Ranch infrastructure. Identified staff and subs.	Excellent	They provided their approach to selecting the best route for selecting the pipeline.	50.00
	4	Project plan. A project plan is a formal document designed to guide the control and execution of a project. A project plan is the key to a successful project and is the most important document that needs to be created when starting any business project. This should include any special concerns or accommodations needed for a successful project. The plan shall also include methods for planning, organizing, scheduling, coordinating, and administering the total effort. Explain the overall approach to the project.	See detailed response in attachment.	200	Good	150.00	In depth approach and detailed plan	Good	In depth approach and detailed plan	150.00	Adequate	100.00		Good	primary consultant of FPL Solar farming	150.00	Excellent	200.00	Specific knowledge of the project area. Bi-weekly progress meetings. Progressive design approach. Constructability review to manage City budget. 30-80-100 plan submittals. Direct bury vs. HDD. Wetland impacts. Plan sheet set. C&T mapped Glade Cutoff Road utilities. Use of drone technology.	Good	They mentioned that they would use a progressive design approach and would provide 30%, 80% and 100% plan submittals to shorten the design time.	150.00
	5	What does your firm anticipate being the most challenging part of this project?	See detailed response in attachment.	100	Adequate	50.00		Adequate		50.00	Adequate	50.00		Marginal	They would want our legal dept. to do the work for the easements	25.00	Excellent	100.00	Alternate route evaluations based on permits and easements for I-95, FPL ROW/property, LTC Ranch (Midway Glades), and wetlands.	Excellent	Discussed obtaining easement contacts early. Suggested routing around wetlands or using directional bores.	100.00
	6	Provide a listing of firm's current contracts.	See detailed response in attachment.	50	Adequate	25.00		Adequate		25.00	Good	37.50	lists similar projects.	Good	lists similar projects.	37.50	Adequate	25.00	Projects mostly include roads, drainage and sidewalks.	Excellent	They have a current contract with LTC Ranch for roads and utilities. Other projects for the City include roads, sidewalks and	50.00
	7	Please complete and attach Form 330 part I and II for evaluation of qualifications & staff/personnel.	See detailed response in attachment.	100	Adequate	50.00		Adequate		50.00	Adequate	50.00		Adequate		50.00	Good	75.00	Qualified personnel.	Excellent	Highly Qualified personnel.	100.00
	8	Value-added services. This term is used for non-core services, or, all services beyond the identified scope. Does the firm recommend any optional value-added services?	See detailed response in attachment.	50	Good	37.50	Record of implementing cost saving approaches	Good	Record of implementing cost saving approaches	37.50	Adequate	25.00		Adequate		25.00	Excellent	50.00	Field plan modifications "on the fly". ArcGIS Online. Drone Aerials. Daily field reports to City. GPS As-Builts. Field inspection shared with City. Value engineering field changes.	Excellent	They have a working relationship with FPL as a siting consultant. They are currently working on the development project for LTC Ranch.	50.00
	9	Proposed Schedule. Making adjustment for issues that may arise during this project, what is your proposed schedule for this project? This section shall include a detailed breakdown and timelines for achieving the scope of work, with a delineation of assigned staff for each task associated with the project. Also include quality assurance efforts for the data collection and analysis tasks, a process for ensuring that no individual respondents will be identified, and a project timeline. The consultant must have sufficient equipment and personnel for back-up and/or emergencies to assure prompt scheduling and completion of services within the schedule. Final project schedule will be negotiated with awarded firm.	See detailed response in attachment.	100	Adequate	50.00		Adequate		50.00	Excellent	100.00	proposal of 300 days is well under the 480 days that the contract states.	Excellent	proposal of 300 days is well under the 480 days that the contract states.	100.00	Excellent	100.00	Internal meetings weekly. 100% plans by May '21, bid July '21, construction October '21 February '22. Use of Internal Task Management software. Construction cost estimates presented at 30%, 80%, and 100 % submittals. Monthly progress meetings. Presented detailed staff assignments for tasks. Included preliminary Gantt chart.	Good	They went into a lot of detail for staffing and project assignments. Project schedule seemed overly optimistic and doesn't consider delays in obtaining easements and FPL agreements. Also, legal review and City response time can impact the time schedule. They revised their estimated time for completion during their presentation. Overall, they presented a thorough understanding of the project.	75.00
	10	Other Material. Please include any additional material that may assist the City in evaluating the proposals and approach to the project. Pre-printed advertisements, brochures, and promotional material may be attached as additional information, but shall not serve as a substitute for a specific response. Attachment of brochures instead of the written response request will be grounds for disqualification or devaluation. A simple "yes" or "no" answer alone will not be acceptable unless clearly requested; an explanation shall be provided for each question/issue listed in this response outline. However, clarity and brevity of presentation, not length, will be favorably considered.	See detailed response in attachment.	50	Adequate	25.00		Adequate		25.00	Adequate	25.00		Good	Engineering and Survey all done in-house	37.50	Adequate	25.00		Good	They presented a lengthy description of their construction services. They discussed resolving potential piping conflicts and other issues prior to start of construction. They would provide inspection, testing and daily reports as required. They would monitor the progress schedule and schedule regular progress meetings. They would maintain progress As-Builts	37.50
	11	Innovation. Please outline any tools in the firms "toolbox" that can be considered innovative and that have proven to benefit the successful completion of similar projects recently.	See detailed response in attachment.	50	Adequate	25.00		Adequate		25.00	Adequate	25.00		Adequate		25.00	Good	37.50	3-D modeling, drones, cloud collaboration for internal staff, GIS asset mapping for historical plans.	Adequate		25.00
	12	Company Experience. Please outline and elaborate on your company's experience with projects similar to this project that included residential construction areas, FDOT permitting, Horizontal directional drilling and large diameter force main (24" or larger).	See detailed response in attachment.	100	Good	75.00	Experience with design of the specified area	Good	Experience with design of the specified area	75.00	Good	75.00	similar projects listed	Good	similar projects listed	75.00	Adequate	50.00	Limited experience with large diameter pipes.	Excellent	Although their experience with large diameter pipe projects for the City were a little more than 5 years ago, they have done quality work on large diameter pipelines in the past.	100.00

Master Technical Evaluation Template

RFP #: 20210022  
 RFP Name: Design & Permitting of the Western 30" & 24" Raw Water  
 Issuing Officer: Jason Bezak  
 Date Reviewed:

Reminder - Do not change formulas in Validated Score columns.

Offeror Name  
 Kimley-Horn and Associates, Inc.

Average Initial Rating 645.83  
 Average Validated Score 716.67

Question and Point information entered in columns A - C will flow to other tabs. Evaluator names will flow to other tabs. Rows 12 thru 18 are hidden on all tabs. Do not unhide these rows. Do not change the formulas on these rows or the spreadsheet will not work.

Question Type	#	Question	Answer	Possible Points	Bilmer Serrano					Daniel Burdett					David Garland							
					Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score
	1	Please provide all documentation needed for Location. Proposer's Location - Location shall mean a business which meets the following criteria: # of Miles from City Hall to Assigned Staff's Office location 0-60 Miles 61-80 Miles 81-100 Miles 101-120 Miles 121-140 Miles 140+ Miles	47 miles	50	Excellent	50.00	Procurement verified this item.	Excellent	Procurement verified this item.	50.00	Excellent	50.00	Procurement verified this item.	Excellent	Procurement verified this item.	50.00	Excellent	50.00	Procurement verified this item.	Excellent	Procurement verified this item.	50.00
	2	Woman/Veteran/Minority Owned Business. Does the Primary firm hold a Minority Business Certification by the Florida Department of Management Services, as described in section 8 of the document? If so, please attach.	No	100	Poor	0.00	Not a Woman/Veteran/Minority owned Business.	Poor	Not a Woman/Veteran/Minority owned Business.	0.00	Poor	0.00	Not a Woman/Veteran/Minority owned Business.	Poor	Not a Woman/Veteran/Minority owned Business.	0.00	Poor	0.00	Not a Woman/Veteran/Minority owned Business.	Poor	Not a Woman/Veteran/Minority owned Business.	0.00
	3	Executive summary. This section should include the Firm's overall concept of the working relationship that will be required to successfully complete this project. The proposer shall provide an executive summary narrative containing information that indicates an understanding of the overall need for and purpose of the services presented in the RFP.	File #4	50	Adequate	25.00		Excellent	Firm has integral knowledge of planned activities of the neighboring parcels and direct contact with necessary sources needed in easement process. Firm has experience obtaining easements within the	50.00	Adequate	25.00		Adequate		25.00	Excellent	50.00	Depth of experience with City. Familiarity with project location. Extensive working experience with large diameter piping.	Excellent	They have excellent qualifications and they are currently working with LTC Ranch on the utilities for the project.	50.00
	4	Project plan. A project plan is a formal document designed to guide the control and execution of a project. A project plan is the key to a successful project and is the most important document that needs to be created when starting any business project. This should include any special concerns or accommodations needed for a successful project. The plan shall also include methods for planning, organizing, scheduling, coordinating, and administering the total effort. Explain the overall approach to the project.	File #4	200	Good	150.00	Good in depth breakdown of required benchmarks	Good	Good in depth breakdown of required benchmarks	150.00	Excellent	200.00	recent experience with Northport Force main	Excellent	Lead Civil engineer for Land Owners, Already has pipe on survey; 's for 2 years. They can expedient easements needed. Also would open cut wetlands.	200.00	Excellent	200.00	Very detailed plan describing key staff responsibilities. Further discussion with keen insight of the coordinated efforts with the City during all phases of the project. Excellent project manager.	Excellent	Because of their working relationship with LTC Ranch they will be able to consult with them and get quick responses for any changes to the pipe route. They are also working with FPL to provide electric power to LTC Ranch. They will address any route changes considering pipeline	200.00
	5	What does your firm anticipate being the most challenging part of this project?	File #4	100	Adequate	50.00		Adequate		50.00	Good	75.00	recent experience will help with challenges	Good	recent experience will help with challenges	75.00	Good	75.00	Discussed pipeline easements for the pipe route. Mentioned wetlands and HDD under-95 and FPL areas.	Excellent	They mentioned the possible use of directional boring under wetlands. During presentation they expressed the opinion that they could do most of the pipeline by open cut. They have prepared plans for FPL Consent Agreement and have already addressed solutions for	100.00
	6	Provide a listing of firm's current contracts.	File #4	50	Adequate	25.00		Adequate		25.00	Excellent	50.00	currently working at JEA WTP	Excellent	currently working at JEA WTP	50.00	Excellent	50.00	Contracts with many SE Florida cities including Port St. Lucie,.	Excellent	They have current contracts with LTC Ranch and are also working for PSLUSD on a 24" force main currently.	50.00
	7	Please complete and attach Form 330 part I and II for evaluation of qualifications & staff/personnel.	File #3	100	Adequate	50.00		Adequate		50.00	Adequate	50.00		Adequate		50.00	Excellent	100.00	Qualified staff with excellent experience. Large support staff of 4,500 engineers across the country. Diverse expertise	Excellent	They have a highly qualified staff and access to other technical experts as required.	100.00

8	Value-added services. This term is used for non-core services, or, all services beyond the identified scope. Does the firm recommend any optional value-added services?	File #4	50	Adequate	25.00		Excellent	Firm has integral knowledge of planned activities of the neighboring parcels and direct contact with necessary sources needed in easement process. Firm is the lead design consultant for LTC.	50.00	Good	37.50	connected developer for LTC Property.	Excellent	In house environmental Team.	50.00	Excellent	50.00	Large multi-disciplined firm that provides additional services within their staff without requiring sub-consultants for majority of the work. Experts at cost saving. Hydraulic model capability. Working relationship with LTC Ranch.	Excellent	They have a working relationship with the attorney for LTC Ranch which will be required to obtain easements from LTC Ranch. Their relationship with FPL to obtain electrical power for this development will be an asset to acquire the easements from the two key players in	50.00
9	Proposed Schedule. Making adjustment for issues that may arise during this project, what is your proposed schedule for this project?  This section shall include a detailed breakdown and timelines for achieving the scope of work, with a delineation of assigned staff for each task associated with the project. Also include quality assurance efforts for the data collection and analysis tasks, a process for ensuring that no individual respondents will be identified, and a project timeline. The consultant must have sufficient equipment and personnel for back-up and/or emergencies to assure prompt scheduling and completion of services within the schedule. *Final project schedule will be negotiated with awarded firm.	File #4	100	Adequate	50.00		Adequate		50.00	Poor	0.00	schedule is showing 536 days, contract calls for 480 days.	Good	Schedule is 460-480 days.	75.00	Marginal	25.00	Short general schedule. Staff assignments answered in other questions.	Good	They provided a short concise schedule mentioning design, permits, easements, legal review, bidding and construction. In their presentation they mentioned that they have all the needed engineering services within their company and can provide quick responses. Because they are the lead engineer for LTC Ranch and have already provided the layout for the pipeline to FPL, they will be able to address easements in a short	75.00
10	Other Material. Please include any additional material that may assist the City in evaluating the proposals and approach to the project. Pre-printed advertisements, brochures, and promotional material may be attached as additional information, but shall not serve as a substitute for a specific response. Attachment of brochures instead of the written response request will not be grounds for disqualification or devaluation. A simple "yes" or "no" answer alone will not be acceptable unless clearly requested; an explanation shall be provided for each question/issue listed in this response outline. However, clarity and brevity of presentation, not length, will be favorably considered.	File #4	50	Good	37.50	Utilizing design-to-operation personnel	Excellent	Firm has integral knowledge of planned activities of the neighboring parcels and direct contact with necessary sources needed in easement process. Firm will use the same design staff through construction to provide continuity to	50.00	Adequate	25.00		Adequate		25.00	Good	37.50	Design team follows project through the construction phase. They provide construction inspection as needed. QC is a key principle. During the bid phase they review shop dwgs and pay requests.	Excellent	Talked about construction experience. They have current projects with LTC Ranch and have just completed design of a 24" force main on Glades Cutoff Road for PSLUSD.	50.00
11	Innovation. Please outline any tools in the firms "toolbox" that can be considered innovative and that have proven to benefit the successful completion of similar projects recently.	File #4	50	Adequate	25.00		Adequate		25.00	Adequate	25.00		Adequate		25.00	Excellent	50.00	Ability to use video-conferencing to review dwgs and revise them live on the air. Prepares 3D images to show conflict solutions. Developed a lift station performance evaluation program. Firm provides a program for	Adequate		25.00
12	Company Experience. Please outline and elaborate on your company's experience with projects similar to this project that included residential construction areas, FDOT permitting, Horizontal directional drilling and large diameter force main (24" or larger).	File #4	100	Adequate	50.00	Experience coordinating with regulatory agencies	Adequate	Experience coordinating with regulatory agencies	50.00	Good	75.00	experience with city projects	Good	experience with city projects	75.00	Excellent	100.00	Experience with FPL and a former employee is on staff. Recent design of Glades Cutoff Road 24" FM required County, DOT and FDEP permits. Experience with HDD of large diameter pipes.	Excellent	They have local experience with FDOT and FPL. They listed several recent projects involving large diameter pipelines and HDD under interstate roads, FPL ROW, and local streets. They are currently the lead engineer for LTC	100.00

Master Technical Evaluation Template

RFP #: 20210022  
 RFP Name: Design & Permitting of the Western 30" & 24" Raw Water  
 Issuing Officer: Jason Bezak  
 Date Reviewed:

Reminder - Do not change formulas in Validated Score columns.

Offeror Name
NOT SHORTLISTED - Chen Moore and Associates

Average Initial Rating	587.50
Average Validated Score	587.50

Question and Point information entered in columns A - C will flow to other tabs. Evaluator names will flow to other tabs. Rows 12 thru 18 are hidden on all tabs. Do not unhide these rows. Do not change the formulas on these rows or the spreadsheet will not work.

Question Type	#	Question	Answer	Possible Points	Bilmer Serrano					Daniel Burdett					David Garland							
					Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score
	1	Please provide all documentation needed for Location. Proposer's Location - Location shall mean a business which meets the following criteria: # of Miles from City Hall to Assigned Staff's Office location 0-60 Miles 61-80 Miles 81-100 Miles 101-120 Miles 121-140 Miles 140+ Miles	0-60 miles	50	Excellent	50.00	48 miles from City Hall.			50.00	Excellent	50.00	48 miles from City Hall.			50.00	Excellent	50.00	48 miles from City Hall.			50.00
	2	Woman/Veteran/Minority Owned Business. Does the Primary firm hold a Minority Business Certification by the Florida Department of Management Services, as described in section 8 of the document? If so, please attach.	No	100	Poor	0.00	Not a Minority Business.			0.00	Poor	0.00	Not a Minority Business.			0.00	Poor	0.00	Not a Minority Business.			0.00
	3	Executive summary. This section should include the Firm's overall concept of the working relationship that will be required to successfully complete this project. The proposer shall provide an executive summary narrative containing information that indicates an understanding of the overall need for and purpose of the services presented in the RFP.	File 4	50	Adequate	25.00				25.00	Good	37.50	long working relationship with PSL			37.50	Good	37.50	Local experience by sub-consultants. Survey & geotech -OK. Firm has good experience with large diameter pipe design. They understand project scope but lack local experience.			37.50
	4	Project plan. A project plan is a formal document designed to guide the control and execution of a project. A project plan is the key to a successful project and is the most important document that needs to be created when starting any business project. This should include any special concerns or accommodations needed for a successful project. The plan shall also include methods for planning, organizing, scheduling, coordinating, and administering the total effort. Explain the overall approach to the project.	File 4	200	Adequate	100.00				100.00	Excellent	200.00	well defined project plan			200.00	Good	150.00	They have an excellent plan for the pipeline design. But have no knowledge of local conditions and no awareness of LTC Ranch. They do not understand that we don't use ductile iron pipe.			150.00
	5	What does your firm anticipate being the most challenging part of this project?	File 4	100	Adequate	50.00				50.00	Excellent	100.00	valid concerns raised with I 95			100.00	Adequate	50.00	They expect the I-95 bore and the pipeline route through the FPL corridor will be the greatest challenges. They are not aware of the wetlands in the area.			50.00
	6	Provide a listing of firm's current contracts.	File 4	50	Adequate	25.00				25.00	Adequate	25.00				25.00	Excellent	50.00	They have a large number of pipeline projects in Broward County and south.			50.00
	7	Please complete and attach Form 330 part I and II for evaluation of qualifications & staff/personnel.	File 4	100	Adequate	50.00				50.00	Adequate	50.00				50.00	Excellent	100.00	They have a large qualified staff.			100.00
	8	Value-added services. This term is used for non-core services, or, all services beyond the identified scope. Does the firm recommend any optional value-added services?	File 4	50	Adequate	25.00				25.00	Adequate	25.00				25.00	Good	37.50	Value engineering cost check throughout construction phase. GIS services to provide data throughout design and construction. Update GIS data to record piping layout during actual installation.			37.50
	9	Proposed Schedule. Making adjustment for issues that may arise during this project, what is your proposed schedule for this project?  This section shall include a detailed breakdown and timelines for achieving the scope of work, with a delineation of assigned staff for each task associated with the project. Also include quality assurance efforts for the data collection and analysis tasks, a process for ensuring that no individual respondents will be identified, and a project timeline. The consultant must have sufficient equipment and personnel for back-up and/or emergencies to assure prompt scheduling and completion of services within the schedule. *Final project schedule will be negotiated with awarded firm.	File 4	100	Adequate	50.00				50.00	Poor	0.00	proposed schedule is 606 days, contract states 480 days.			0.00	Marginal	25.00	Didn't address all of the question. No mention of staff assignments. Provided Gantt chart project timeline.			25.00
	10	Other Material. Please include any additional material that may assist the City in evaluating the proposals and approach to the project. Pre-printed advertisements, brochures, and promotional material may be attached as additional information, but shall not serve as a substitute for a specific response. Attachment of brochures instead of the written response request will be grounds for disqualification or devaluation. A simple "yes" or "no" answer alone will not be acceptable unless clearly requested; an explanation shall be provided for each question/issue listed in this response outline. However, clarity and brevity of presentation, not length, will be favorably considered.	File 4	50	Good	37.50	Schedule timeline of process submitted			37.50	Adequate	25.00				25.00	Adequate	25.00	Details of their QC procedures.			25.00
	11	Innovation. Please outline any tools in the firms "toolbox" that can be considered innovative and that have proven to benefit the successful completion of similar projects recently.	File 4	50	Adequate	25.00				25.00	Adequate	25.00				25.00	Good	37.50	BoreAid HDD software. Staff has certification in HDPE pipe fusion.			37.50
	12	Company Experience. Please outline and elaborate on your company's experience with projects similar to this project that included residential construction areas, FDOT permitting, Horizontal directional drilling and large diameter force main (24" or larger).	File 4	100	Good	75.00	Experience with horizontal directional drilling in various projects			75.00	Adequate	50.00				50.00	Excellent	100.00	Experienced in piping projects in residential neighborhoods. Many HDD projects with large diameter pipes. Great table provided showing projects and identifying owner and agencies involved including FDOT, FPL, FDEP, SFWMD, and other local agencies.			100.00



**Master Technical Evaluation Template**

RFP #: 20210022  
 RFP Name: Design & Permitting of the Western 30" & 24" Raw Water  
 Issuing Officer: Jason Bezak  
 Date Reviewed:

Reminder - Do not change formulas in Validated Score columns.

<b>Offeror Name</b>	<b>Average Initial Rating</b>	<b>612.50</b>
<b>NOT SHORTLISTED - CivilSurv Design Group, Inc.</b>	<b>Average Validated Score</b>	<b>612.50</b>

**Question and Point information entered in columns A - C will flow to other tabs. Evaluator names will flow to other tabs. Rows 12 thru 18 are hidden on all tabs. Do not unhide these rows. Do not change the formulas on these rows or the spreadsheet will not work.**

Question Type	#	Question	Answer	Possible Points	Bilmer Serrano					Daniel Burdett					David Garland							
					Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score
	1	Please provide all documentation needed for Location. Proposer's Location - Location shall mean a business which meets the following criteria: # of Miles from City Hall to Assigned Staff's Office location 0-60 Miles 61-80 Miles 81-100 Miles 101-120 Miles 121-140 Miles 140+ Miles	CivilSurv's office is located within 0-60 Miles of City Hall. Please refer to Page 14 of File #4.	50	Excellent	50.00	PMD verified Location.			50.00	Excellent	50.00	PMD verified Location.			50.00	Excellent	50.00	PMD verified Location.			50.00
	2	Woman/Veteran/Minority Owned Business. Does the Primary firm hold a Minority Business Certification by the Florida Department of Management Services, as described in section 8 of the document? If so, please attach.	No, CivilSurv does not hold this certification.	100	Poor	0.00	PMD verified CivilSurv is not WBE, MBE or Veteran Owned business.			0.00	Poor	0.00	PMD verified CivilSurv is not WBE, MBE or Veteran Owned business.			0.00	Poor	0.00	PMD verified CivilSurv is not WBE, MBE or Veteran Owned business.			0.00
	3	Executive summary. This section should include the Firm's overall concept of the working relationship that will be required to successfully complete this project. The proposer shall provide an executive summary narrative containing information that indicates an understanding of the overall need for and purpose of the services presented in the RFP.	Please refer to the Executive Summary on Page 17 of File #4.	50	Adequate	25.00				25.00	Adequate	25.00				25.00	Good	37.50	Firm has good understanding of the project and familiar with the location and challenges.			37.50
	4	Project plan. A project plan is a formal document designed to guide the control and execution of a project. A project plan is the key to a successful project and is the most important document that needs to be created when starting any business project. This should include any special concerns or accommodations needed for a successful project. The plan shall also include methods for planning, organizing, scheduling, coordinating, and administering the total effort. Explain the overall approach to the project.	Please refer to the Project Plan on Page 18 of File #4.	200	Good	150.00	In depth approach to all critical steps			150.00	Good	150.00	very extensive project plan, breaks down entire project.			150.00	Excellent	200.00	Well thought-out plan. Knowledge of permits and required easements. Good experience with FPL. Discussed QC and cost control.			200.00
	5	What does your firm anticipate being the most challenging part of this project?	Please refer to the Anticipated Project Challenges on Page 23 of File #4.	100	Adequate	50.00				50.00	Adequate	50.00				50.00	Excellent	100.00	FPL response time and experience with them. Discussed easements and possible delays.			100.00
	6	Provide a listing of firm's current contracts.	Please refer to the Current Contracts List on Page 24 of File #4.	50	Adequate	25.00				25.00	Adequate	25.00				25.00	Good	37.50	Contracts with several counties and FPL.			37.50
	7	Please complete and attach Form 330 part I and II for evaluation of qualifications & staff/personnel.	Please refer to File #3 for SF330 information. (pages 25-49 of File #4)	100	Good	75.00	Experience with existing system			75.00	Adequate	50.00				50.00	Good	75.00	Good team with local experience.			75.00
	8	Value-added services. This term is used for non-core services, or, all services beyond the identified scope. Does the firm recommend any optional value-added services?	Please refer to the Value-Added Services information on Page 50 of File #4.	50	Adequate	25.00				25.00	Adequate	25.00				25.00	Excellent	50.00	Geotech expert. Hydraulic analysis. FDOT existing survey. SUE staff in-house.			50.00
	9	Proposed Schedule. Making adjustment for issues that may arise during this project, what is your proposed schedule for this project?  This section shall include a detailed breakdown and timelines for achieving the scope of work, with a delineation of assigned staff for each task associated with the project. Also include quality assurance efforts for the data collection and analysis tasks, a process for ensuring that no individual respondents will be identified, and a project timeline. The consultant must have sufficient equipment and personnel for back-up and/or emergencies to assure prompt scheduling and completion of services within the schedule. *Final project schedule will be negotiated with awarded firm.	Please refer to the Proposed Schedule on Pages 51 and 52 of File #4.	100	Good	75.00	In depth breakdown and specific schedule of all critical benchmarks			75.00	Poor	0.00	proposing a 593 day schedule, contract calls for 480 days.			0.00	Adequate	50.00	Thorough discussion of staff assignments. Qualified staff for various tasks and unexpected problems. Detailed Gant chart.			50.00
	10	Other Material. Please include any additional material that may assist the city in evaluating the proposals and approach to the project. Pre-printed advertisements, brochures, and promotional material may be attached as additional information, but shall not serve as a substitute for a specific response. Attachment of brochures instead of the written response request will be grounds for disqualification or devaluation. A simple "yes" or "no" answer alone will not be acceptable unless clearly requested; an explanation shall be provided for each question/issue listed in this response outline. However, clarity and brevity of presentation, not length, will be favorably considered.	Please refer to Other Material on Page 53 of File #4.	50	Adequate	25.00				25.00	Adequate	25.00				25.00	Good	37.50	Change order and claims experience with negotiations. Cost control. Alternative delivery. Constructability.			37.50
	11	Innovation. Please outline any tools in the firms "toolbox" that can be considered innovative and that have proven to benefit the successful completion of similar projects recently.	Please refer to Innovation on Page 56 of File #4.	50	Adequate	25.00				25.00	Adequate	25.00				25.00	Adequate	25.00				25.00
	12	Company Experience. Please outline and elaborate on your company's experience with projects similar to this project that included residential construction areas, FDOT permitting, Horizontal directional drilling and large diameter force main (24" or larger).	Please refer to Company Experience on Page 57 of File #4.	100	Excellent	100.00	Experience with existing system expansion project			100.00	Adequate	50.00				50.00	Good	75.00	Mentioned previously. HDD experience.			75.00

Master Technical Evaluation Template

RFP #: 20210022  
 RFP Name: Design & Permitting of the Western 30" & 24" Raw Water  
 Issuing Officer: Jason Bezak  
 Date Reviewed:

Reminder - Do not change formulas in Validated Score columns.

Offeror Name
NOT SHORTLISTED - Holtz Consulting Engineers, Inc.

Average Initial Rating	591.67
Average Validated Score	591.67

Question and Point information entered in columns A - C will flow to other tabs. Evaluator names will flow to other tabs. Rows 12 thru 18 are hidden on all tabs. Do not unhide these rows. Do not change the formulas on these rows or the spreadsheet will not work.

Question Type	#	Question	Answer	Possible Points	Bilmer Serrano					Daniel Burdett					David Garland							
					Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score	Initial Rating	Initial Score	Initial Comments	Validated Rating	Validated Comments	Validated Score
	1	Please provide all documentation needed for Location. Proposer's Location - Location shall mean a business which meets the following criteria: # of Miles from City Hall to Assigned Staff's Office location 0-60 Miles 61-80 Miles 81-100 Miles 101-120 Miles 121-140 Miles 140+ Miles	0-60	50	Excellent	50.00	Within 10 miles of City Hall. Verified by Procurement.			50.00	Excellent	50.00	Within 10 miles of City Hall. Verified by Procurement.			50.00	Excellent	50.00	Within 10 miles of City Hall. Verified by Procurement.			50.00
	2	Woman/Veteran/Minority Owned Business. Does the Primary firm hold a Minority Business Certification by the Florida Department of Management Services, as described in section 8 of the document? If so, please attach.	YES	100	Excellent	100.00	Verified as a Minority Business.			100.00	Excellent	100.00	Verified as a Minority Business.			100.00	Excellent	100.00	Verified as a Minority Business.			100.00
	3	Executive summary. This section should include the Firm's overall concept of the working relationship that will be required to successfully complete this project. The proposer shall provide an executive summary narrative containing information that indicates an understanding of the overall need for and purpose of the services presented in the RFP.	YES	50	Adequate	25.00			25.00	Adequate	25.00			25.00	Good	37.50			Well organized summary detailing capabilities of firm and their understanding of the project challenges.			37.50
	4	Project plan. A project plan is a formal document designed to guide the control and execution of a project. A project plan is the key to a successful project and is the most important document that needs to be created when starting any business project. This should include any special concerns or accommodations needed for a successful project. The plan shall also include methods for planning, organizing, scheduling, coordinating, and administering the total effort. Explain the overall approach to the project.	YES	200	Adequate	100.00			100.00	Adequate	100.00			100.00	Excellent	200.00			Discussed design aspects as well as construction services, hydraulic modeling, and evaluation of alternative pipe routes. Also mentioned grant assistance, surveying, easement acquisition, permits, value engineering, constructability review, and bidding services. During construction they would provide periodic site visits			200.00
	5	What does your firm anticipate being the most challenging part of this project?	YES	100	Poor	0.00			0.00	Adequate	50.00			50.00	Adequate	50.00			Mentioned in Executive			50.00
	6	Provide a listing of firm's current contracts.	YES	50	Adequate	25.00			25.00	Good	37.50	currently a consultant for the city		37.50	Good	37.50			Extensive list of projects within SE Florida.			37.50
	7	Please complete and attach Form 330 part I and II for evaluation of qualifications & staff/personnel.	YES	100	Adequate	50.00			50.00	Adequate	50.00			50.00	Good	75.00			Qualified list of highly experienced staff.			75.00
	8	Value-added services. This term is used for non-core services, or, all services beyond the identified scope. Does the firm recommend any optional value-added services?	YES	50	Adequate	25.00			25.00	Adequate	25.00			25.00	Adequate	25.00			Discussed how they can provide their expertise for the project.			25.00
	9	Proposed Schedule. Making adjustment for issues that may arise during this project, what is your proposed schedule for this project?  This section shall include a detailed breakdown and timelines for achieving the scope of work, with a delineation of assigned staff for each task associated with the project. Also include quality assurance efforts for the data collection and analysis tasks, a process for ensuring that no individual respondents will be identified, and a project timeline. The consultant must have sufficient equipment and personnel for back-up and/or emergencies to assure prompt scheduling and completion of services within the schedule. *Final project schedule will be negotiated with awarded firm.	YES	100	Poor	0.00			0.00	Poor	0.00	proposed schedule is not included		0.00	Poor	0.00			Missing schedule, staff assignments, tasks. They forgot to insert the schedule.			0.00
	10	Other materials. Please include any additional material that may assist the City in evaluating the proposals and approach to the project. Pre-printed advertisements, brochures, and promotional material may be attached as additional information, but shall not serve as a substitute for a specific response. Attachment of brochures instead of the written response request will be grounds for disqualification or devaluation. A simple "yes" or "no" answer alone will not be acceptable unless clearly requested; an explanation shall be provided for each question/issue listed in this response outline. However, clarity and brevity of presentation, not length, will be favorably considered.	YES	50	Adequate	25.00			25.00	Adequate	25.00			25.00	Adequate	25.00			They provided reference letters.			25.00
	11	Innovation. Please outline any tools in the firms "toolbox" that can be considered innovative and that have proven to benefit the successful completion of similar projects recently.	YES	50	Adequate	25.00			25.00	Adequate	25.00			25.00	Good	37.50			They have project management software with forms for their internal use to track progress.			37.50
	12	Company Experience. Please outline and elaborate on your company's experience with projects similar to this project that included residential construction areas, FDOT permitting, Horizontal directional drilling and large diameter force main (24" or larger).	YES	100	Good	75.00	Experience with horizontal directional drilling		75.00	Adequate	50.00			50.00	Excellent	100.00			They provided descriptions of comparable projects and also referenced the SF330 Form. Presented a table showing projects that required construction in residential areas, FDOT permitting, horizontal directional drilling, and installation of large diameter piping greater than 24" diameter.			100.00
